


How Kapitol scaled planning, from tenders to delivery with Asta suite solutions

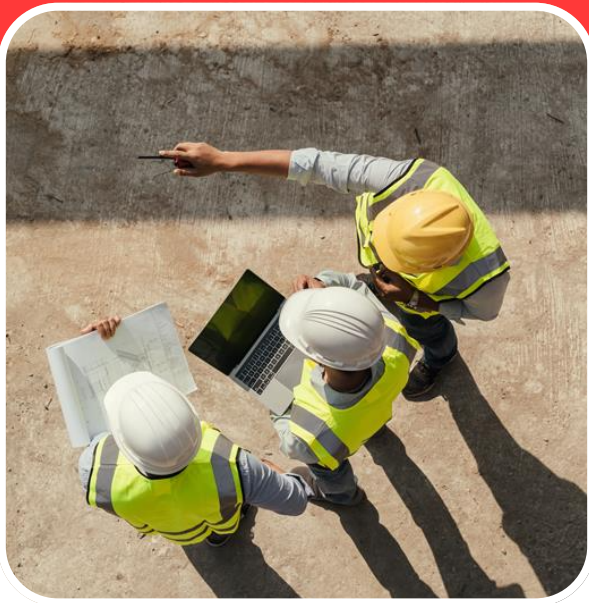

Kapitol uses Asta to underpin both pre-construction planning and live project delivery, supporting over fifty users across the business.

Kapitol is an Australian head contractor operating as a Tier One builder across multiple sectors including data centres and critical infrastructure, residential, commercial, education, sports projects and recently modular. The business runs 10–15 live projects in Asta at any one time, alongside a strong new business pipeline in the state of Victoria and Northern Territory.

Garret Jackson, Planning Manager, joined Kapitol in January 2023 to lead pre-construction planning and to support on-site delivery teams with robust, standardised programmes. With over 10 years' experience using Asta, plus extensive exposure to Oracle Primavera P6 and Microsoft Project, he was tasked with modernising Kapitol's planning tools and workflows.



Key benefits for Kapitol

- ✓ Stronger bids and clearer client communication
- ✓ Single source of truth and portfolio visibility
- ✓ Freed-up Planners and empowered project managers
- ✓ Partnership, support and future readiness



The challenge – finding a scalable solution

Kapitol struggled to keep pace as programmes became more detailed and the projects portfolio grew.

The team needed:

- An intuitive tool that project managers and coordinators could learn quickly, not just the specialist Planners.
- Cloud-based programme management to support multi-project visibility, and portfolio reporting and to be a single source of truth.
- Integration with existing Power BI dashboards so programme performance could sit alongside design, procurement, quality and workplace health & safety reporting.
- A platform that would evolve with the business, including APIs, AI capabilities and mobile progress capture.

At the same time, Kapitól wanted to avoid disruption and “tool fatigue” when moving teams away from familiar software. Any new solution had to be easy to adopt and clearly beneficial for both office and site users.

Drawing on his UK experience, Garret led a review of several alternative options, before recommending Asta as the best fit for Kapitól. After a short internal trial, it became clear that Asta offered the right balance of power, usability and value for money, with a roadmap aligned to Kapitól's digital strategy.

“From a future business perspective, having that one source of truth and the connectivity through APIs and BI is huge.”

Garret Jackson,
Planning Manager



Solution: Asta Vision with Asta Powerproject

The rollout followed a phased approach:

1. Migration: live and historical projects were converted into Asta Powerproject, with new tenders created in Asta from day one.
2. Planner-led foundation: Garret initially used Asta as a standalone tool, building robust templates and standards for both tender and delivery programmes.
3. Transition to the cloud: Kapitól then implemented Asta Vision so programmes could “live” in a controlled, cloud-based environment, forming a single source of truth across the project portfolio.
4. BI integration: Asta Vision was integrated with Power BI, allowing programme data to feed directly into Kapitól's existing dashboard suite alongside design, procurement, quality and workplace health & safety.
5. Enabling project teams: Using Asta Vision, project managers now check out programmes, update status and publish changes back to the central dashboards, with Planners providing auditing and hands-on support where needed.

Comprehensive, tailored training and highly responsive support from the local Asta partner, Solid Support were critical to the change programme. Kapitól's onboarding model gives project managers training first, then access to an Asta licence, building confidence and reducing the perceived leap to new systems.



Adoption and ways of working

What began as a Planner-led initiative has grown into an organisation-wide deployment. Around fifty users now access Asta across Kapitool, including:

- Planning team – new business (1), construction delivery (3).
- Project managers, assistant PMs and project coordinators – responsible for regular status updates and using dashboards in reviews.
- Site teams – using Asta outputs to understand sequence, dates and constraints on live projects.
- Senior management – reviewing weekly performance via Power BI dashboards fed from Asta Vision, with a clear view of project status, remaining work and emerging risks.

Asta Powerproject's ability to import and export Microsoft Project & P6 files means Planners can work natively in Asta while still exchanging programmes in agreed format for clients and partners. This allows Kapitool to support existing Project-based workflows without sacrificing the benefits of its new, Asta-centred planning environment.

“We couldn't take a step back from Asta Vision; if you were to say ‘we're getting rid of that’, it would be a big setback.”

Garret Jackson,
Planning Manager

Why Kapitool recommends Asta:

When peers in the industry ask about planning software, Kapitool's message is clear: Asta provides a one-stop ecosystem for programme management that balances ease of use with enterprise-grade capability. For organisations seeking a single version of the truth, strong BI integration and tools that both Planners and project managers want to use, Asta has proven to be a future-proof choice.

Book a demo

Discover the power behind successful projects: book a free demo today to explore Asta.
Call us on +61 2 9743 4666 or email us at experience@solidsupport.com.au



Impact – from better tenders to smarter delivery

Stronger bids and clearer client communication

For new business, Asta's presentation flexibility is a standout feature. Garret uses high-level dashboard programmes and task-per-line views to produce one-page, branded schedules that clearly tell the story of design, procurement and construction across complex schemes. This has enhanced the quality and impact of Kapitool's tender proposals and supports more compelling conversations with clients at an early stage.

Single source of truth and portfolio visibility

With programmes stored and controlled in Asta Vision, Kapitool now has a single, auditable source of truth for every live project. Controlled editing where Planner manage core logic and PMs update progress protects data integrity while still empowering project teams. Bi-weekly reviews use Power BI dashboards connected to Asta Vision to assess project health, remaining work vs remaining time, and critical path movement across the portfolio.

Freed-up Planners and empowered project managers

By shifting routine progress reporting to project managers via Asta Vision and Asta Site Progress, Planners have been able to focus on higher-value activities such as major programme revisions, scenario planning, risk analysis and improving templates and standards. Clear processes and internal planning guidelines now set out how to check out programmes, update them and complete weekly or bi-weekly reporting. All of these efforts result in raising the planning capability of the whole business.

Partnership, support and future readiness

Kapitool highlights the responsiveness and hands-on nature of both Solid Support and the Elecosoft team, from troubleshooting through to workshops on Asta Vision and APIs. Trial periods for new capabilities, along with training content and user groups, have helped the business adopt features such as Vision and dashboard integration at its own pace.

Looking ahead, Kapitool sees Asta as a platform that can evolve with the industry. Planned and emerging capabilities around APIs, AI and deeper integration with other construction systems will further strengthen the “single source of truth” model and support increasingly data-driven decision making.
